DISTRICT	COUNTY	ROUTE	SECTION		SHEET				
6-0	CHESTER	82	CDR		1 OF 2				
	WEST MARLBOROUGH								
REV NO	REVISIONS	5		DATE	BY	APPD			

## TABULATION OF TRAFFIC CONTROL DEVICES ITEM 0901-0001 (FOR INFORMATION ONLY)


SYM	SERIES	SIZE	AREA EACH SF	REMARKS	TOTAL QTY.	TOTAL AREA SF	TYPE B LIGHT	TYPE III BARR- ICADE
1	W20-2	36 "X36 "		ADVANCE DETOUR	8	72.00		
ı	W30-1-6	20 "X6 "	0.83	DISTANCE (AHEAD)	8	6.64		
	M4-8	24 "X12 "	2.00	DETOUR MARKER	16	32.00		
2	M1-5	24 "X24 "	4.00	PENNSYLVANIA ROUTE MARKER	16	64.00		
	M6-3	21 "X15 "		STRAIGHT THROUGH MARKER	16	35.04	_	
3	R11-3B	48 "X 1 8 "		BRIDGE OUT - LOCAL TRAFFIC ONLY	3	37.50	6	3
	M4-8	24 "X12 "	2.00	DETOUR MARKER	2	4.00		
4	M1-5	24 "X24 "	4.00	PENNSYLVANIA ROUTE MARKER	2	8.00		_
	M5-1L	21 "X15 "	2.19	ADVANCE 90 DEGREE LEFT TURN	2	4.38		
	M4-8	24 "X12 "	2.00	DETOUR MARKER	6	12.00		
5	M1-5	24 "X24 "		PENNSYLVANIA ROUTE MARKER	6	24.00		
	M6-1L	21 "X15 "	2.19	90 DEGREE LEFT TURN	6	13.14		
	M4-8	24 "X12 "	2.00	DETOUR MARKER	6	12.00		
6	M1-5	24 "X24 "	4, 00	PENNSYLVANIA ROUTE MARKER	6	24.00		
	M6-1R	21 "X15 "	2.19	90 DEGREE RIGHT TURN	6	13.14		
_	M4-8	24 "X12 "	2.00	DETOUR MARKER	7	14.00		
7	M1-5	24 "X24 "		PENNSYLVANIA ROUTE MARKER	7	28.00		
	M5 - 1R	21 "X15 "		ADVANCE 90 DEGREE LEFT TURN	7	15.33	_	
8	W20-3	36 "X36 "		ROAD CLOSED	5	45.00		
	W30-1-6	20 "X6 "		DISTANCE (AHEAD)	5	4. 15	5	
9	M1-5	24 "X24 "		PENNSYLVANIA ROUTE MARKER	2	8.00		
	M4-8A	24 "X18 "		END DETOUR	2	6.00		
10	R-11-2-1	48 "X30"		BRIDGE CLOSED		70.00	14	7
<u> </u>	M4-10R	48 "X18 "	6.00	DETOUR ARROW (RIGHT)	2	12.00		
В	M4-10L	48 "X18 "	6.00	DETOUR ARROW (LEFT)	2	12.00		
С	M3-1	24 "X12 "	2.00	NORTH MARKER	23	46.00		
D	M3-3	24 "X12 "	2.00	SOUTH MARKER	13	26.00		
		TOTAL	99.61		191.00	648.32	25.00	10.00

## TABULATION OF TRAFFIC CONTROL ITEMS

MAINTENANCE AND PROTECTION OF TRAFFIC DURING CONSTRUCION		ADDITIONAL WARNING LIGHTS, TYPE B		ADDITIONAL TRAFFIC CONTROL SIGNS		
0901	۲S	0901 0231	DAY	0901 0240	SF	
$\geq$		100		100	)	ENTIRE PROJECT

RECOMMENDED
ASSISTANT DISTRICT TRAFFIC ENGINEER


TRAFFIC CONTROL PLAN

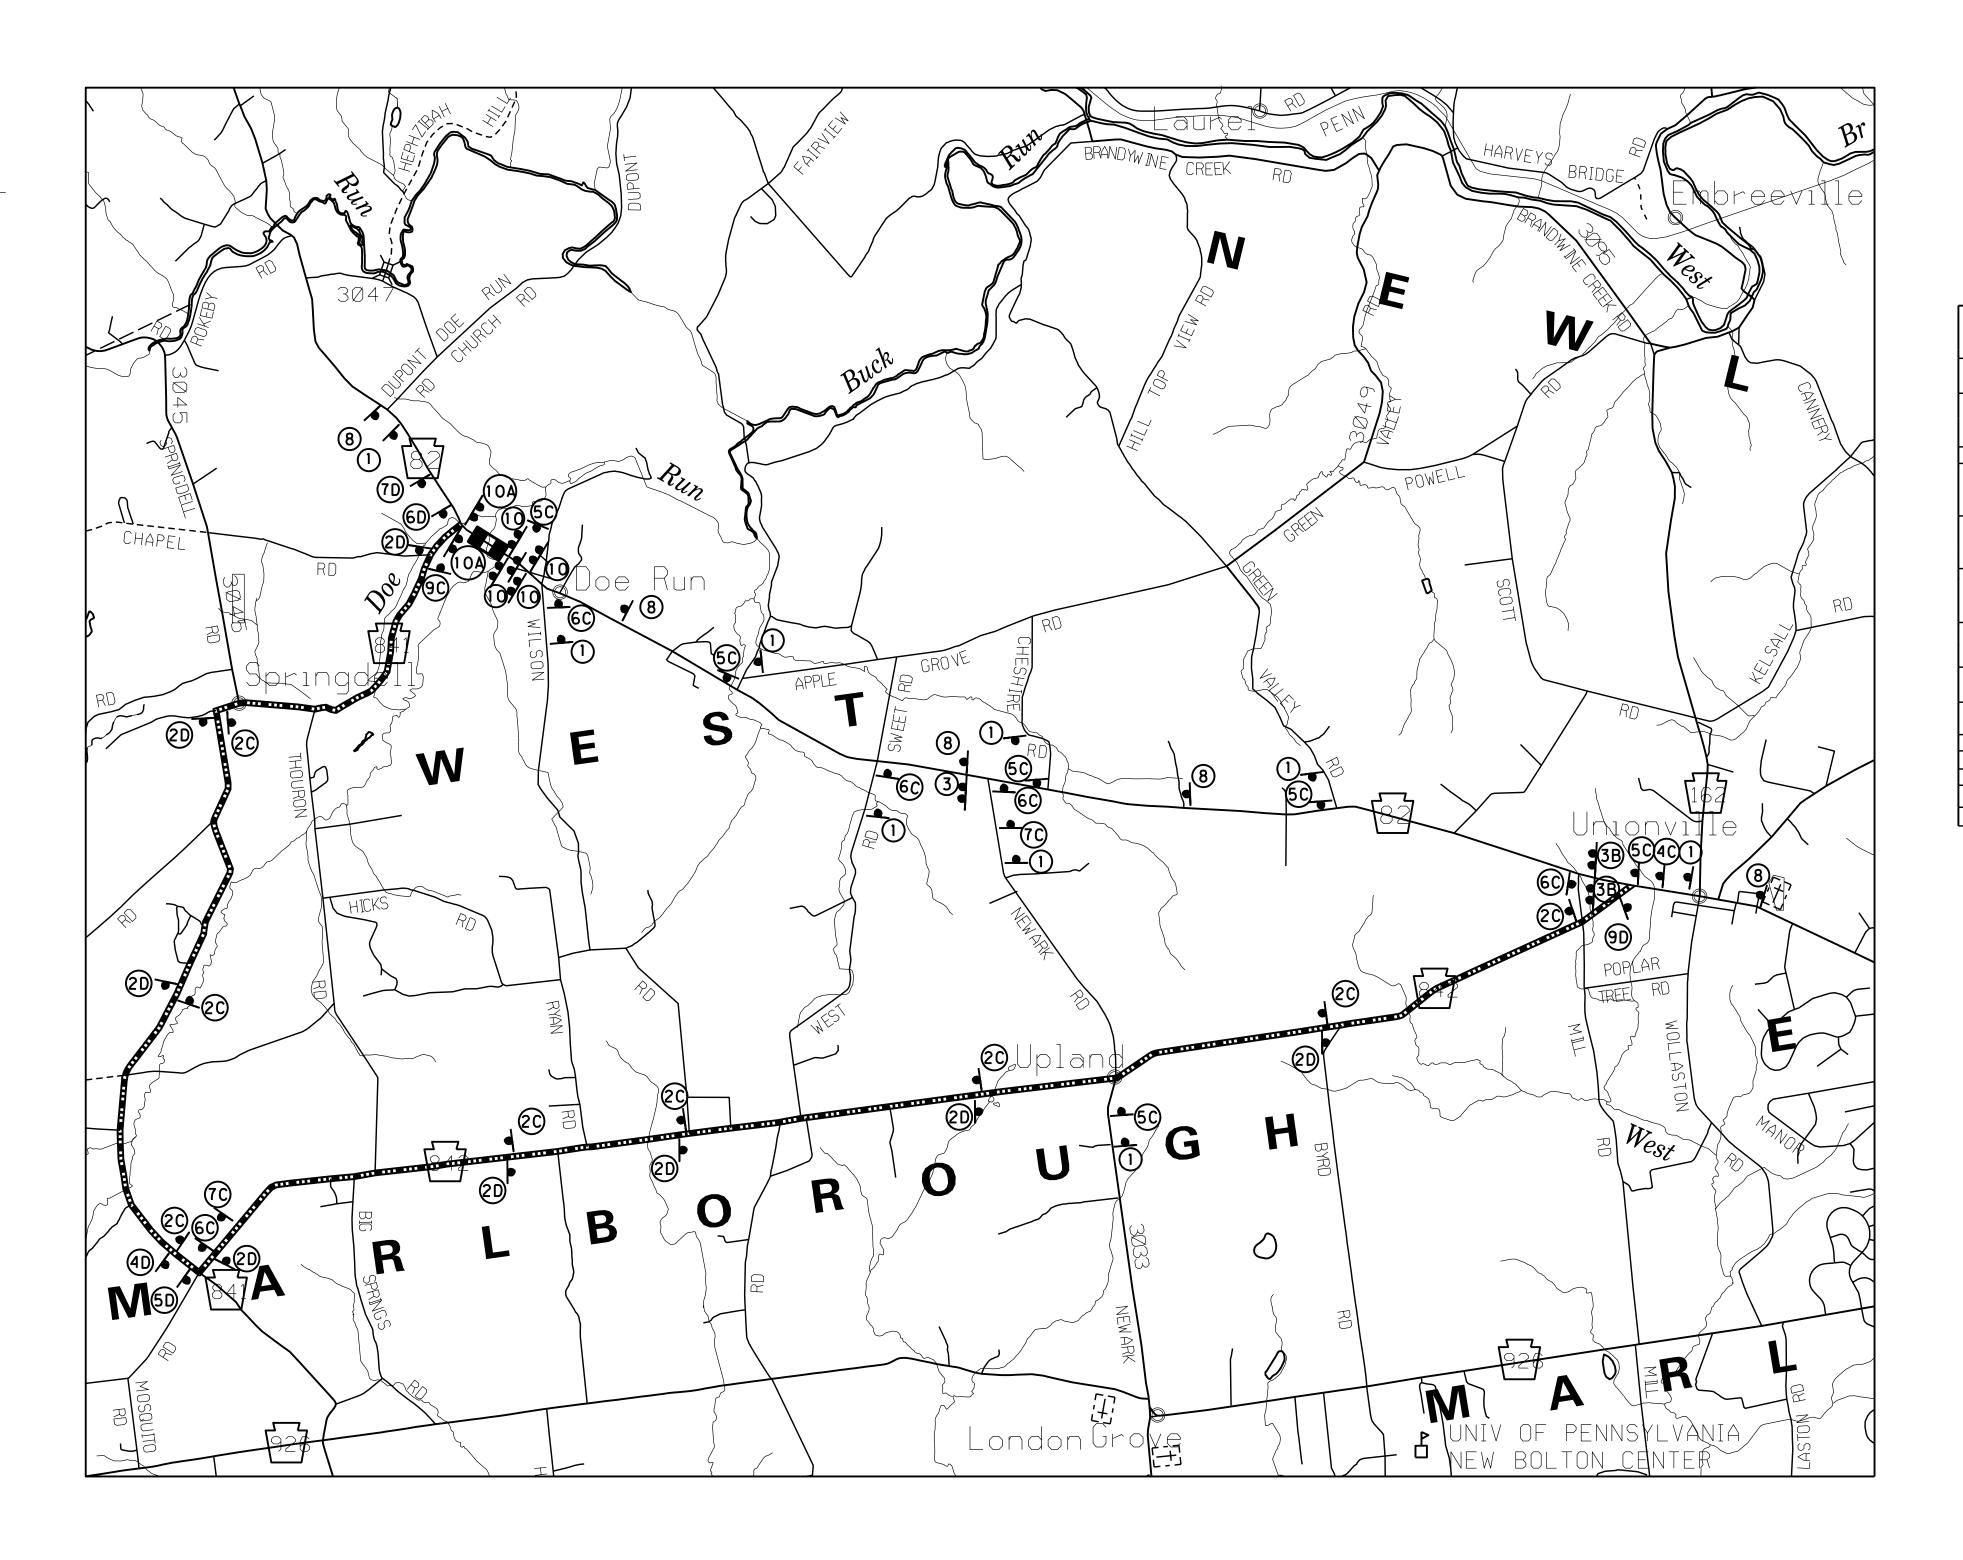

2 MILE

**LEGEND** <u>SCALE</u> DETOUR ROUTE PROJECT LOCATION 0.0

SIGN ON TYPE III BARRICADE

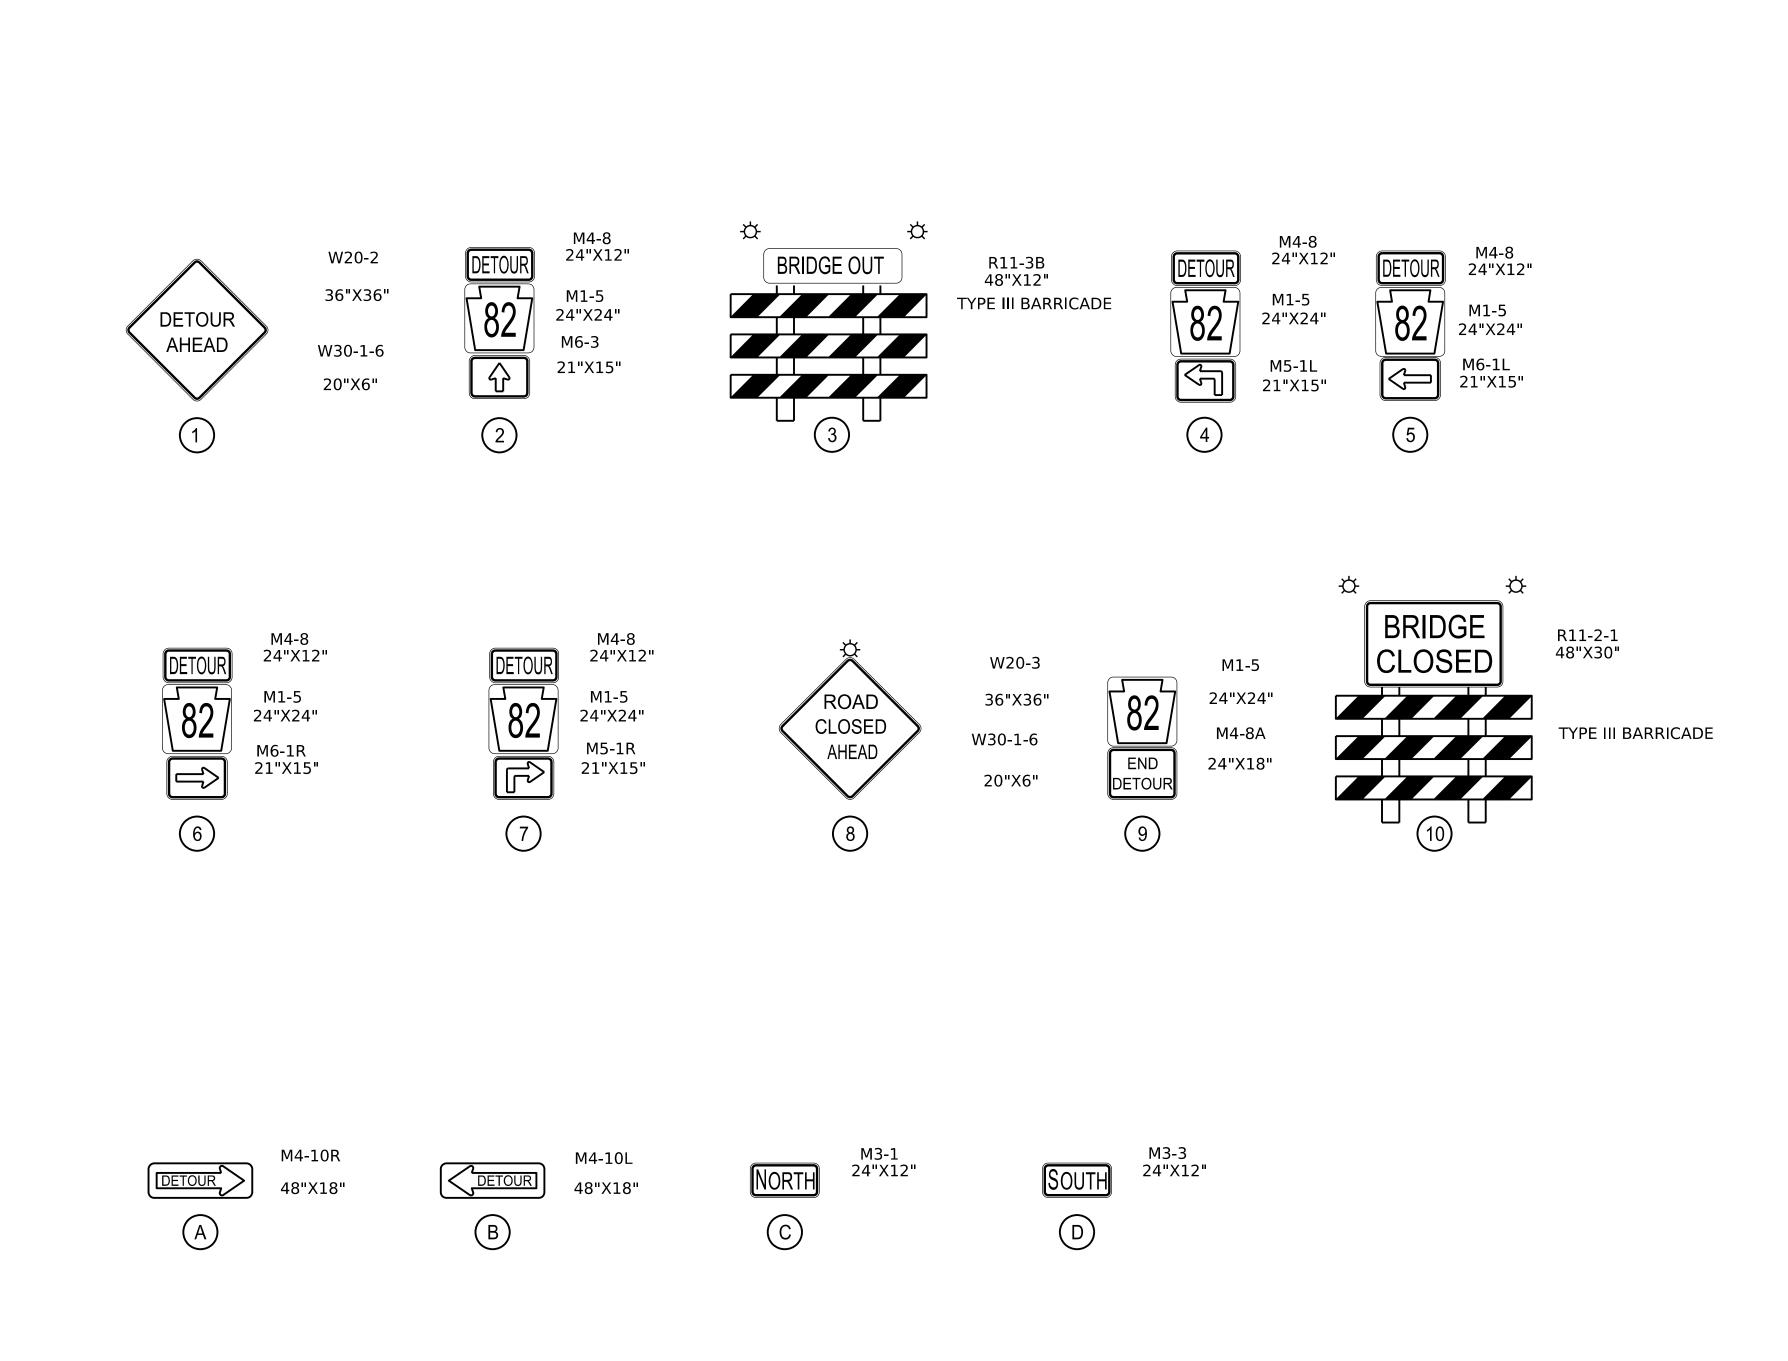

DISTRICT	COUNTY	ROUTE	SECTION	SHEET					
6-0	CHESTER	82	CDR	2 0	F 2				
WEST MARLBOROUGH									
REV	REVISIONS	DAT	F BY	ΔPPD					

	WEST MAREBOROUGH								
F	REV NO	REVISIONS	DATE	BY	APPD				

## **GENERAL NOTES**

THIS WORK CONSISTS OF THE MAINTENANCE OF TRAFFIC AND THE PROTECTION OF THE TRAVELING PUBLIC APPROACHING THE CONSTRUCTION AREA AND WITHIN THE LIMITS OF CONSTRUCTION.

FURNISH, ERECT, PLACE, AND MAINTAIN TRAFFIC CONTROL SIGNS AND DEVICES AND MAINTAIN TRAFFIC DURING HOURS OF CONSTRUCTION AND AT ALL OTHER TIMES IN ACCORDANCE WITH THE METHODS INDICATED ON THESE DRAWINGS AND,

- 1. THE SPECIAL PROVISIONS OF THE CONTRACT,
- 2. PA CODE, TITLE 67, CHAPTER 212, OFFICIAL TRAFFIC CONTROL DEVICES,
- 3. PDT PUBLICATION NO. 213, TEMPORARY TRAFFIC CONTROL GUIDELINES,
- 4. FHWA MANUAL ON UNIFORM TRAFFIC CONTROL
- DEVICES,
  5. PDT PUBLICATION NO. 35, APPROVED
- CONSTRUCTION MATERIALS (BULLETIN 15), 6. PDT PUBLICATION NO. 408, SPECIFICATIONS,
- 7. PDT PUBLICATION 111, TRAFFIC CONTROL -
- PAVEMENT MARKINGS AND SIGNING STANDARDS.

IMMEDIATELY UPON COMPLETION OF THE WORK, REMOVE THE DEVICES.THE DEPARTMENT WILL REMOVE ANY TRAFFIC CONTROL DEVICES ERECTED BY DEPARTMENT FORCES.

THE ENGINEER WILL INSPECT ALL TRAFFIC CONTROL DEVICES PRIOR TO START OF WORK.

COVER OR REMOVE ALL SIGNS NOT IN USE. DO NOT PLACE TAPE ON THE FACE OF ANY SIGN.

IN ADDITION TO MINIMUM VERTICAL CLEARANCE REQUIREMENTS, INSTALL SIGNS WITHIN UNPROTECTED AREAS SO THAT THE TOP IS NO LESS THAN NINE FEET ABOVE GRADE. SIGNS MOUNTED ON PORTABLE SUPPORTS FOR SHORT-TERM OPERATIONS ARE EXCLUDED.

USE TYPE III OR BETTER RETROREFLECTIVE SHEETING ON ALL LONG-TERM SIGNS AND TYPE III BARRICADE RAILS, UNLESS OTHERWISE NOTED.

DO NOT USE AUTOMATED FLAGGER ASSISTING DEVICES (AFAD) AS A TRAFFIC CONTROL DEVICE UNLESS OTHERWISE APPROVED IN WRITING BY THE DISTRICT TRAFFIC ENGINEER.
